


PLYMOUTH TOWN HALL PROJECT UPDATE

Demolition/Construction Issues: Contact-

Plymouthconstructionmitigation@stvinc.com or 617-480-8645

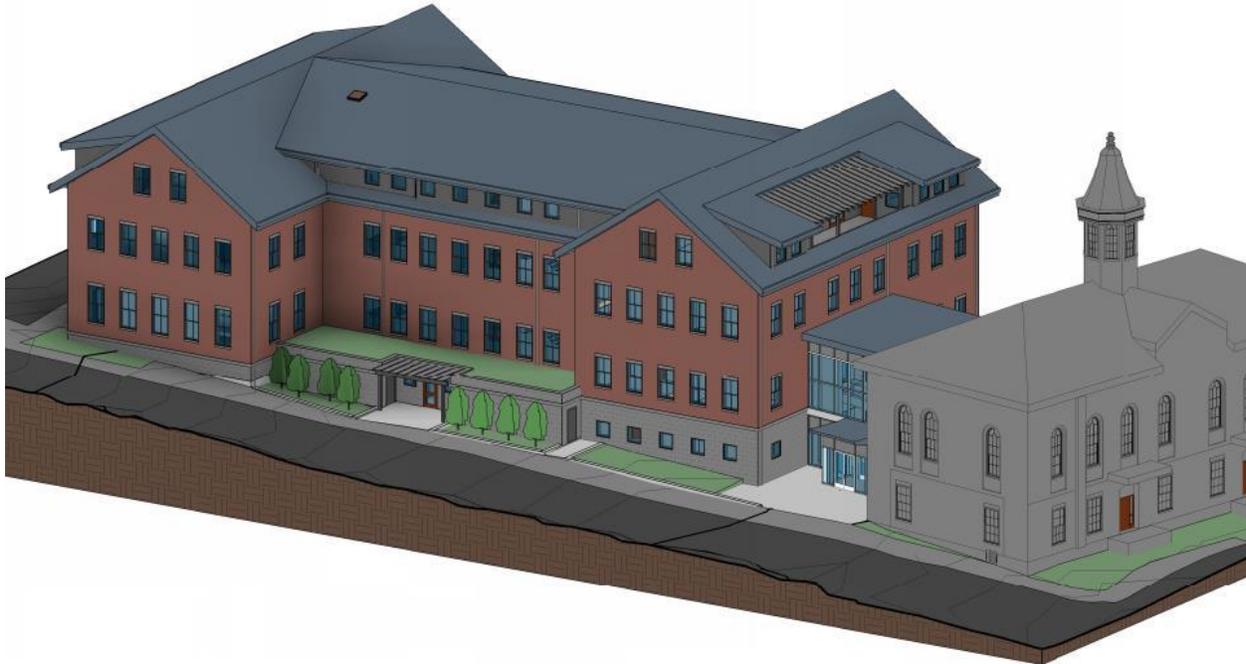

TOWN HALL
CONCEPTUAL RENDERING
SOUTH RUSSELL STREET

Project Statement:



The Town of Plymouth is embarking on an exciting project that will provide the community with a new Town Hall including a renovated 1820 Courthouse. The Project is located at 26 Court Street and consists of two phases. Phase I is the demolition of the old Police Station (DPW Sign Shop), the Commissioner's Building, and later additions to the 1820 Courthouse.


Milestone Project Schedule:

Phase I- Demolition Activities	Late-January 2015 through Early-April 2015
Roadway Utility Improvements	Early-April through Late-May 2015
Phase II- Town Hall Construction	Fall 2015 through Summer 2017
Roadway Repaving	Fall 2017

Traffic, Parking and Site Utilization:

As with any major construction project, there will be impacts to neighbors and surrounding areas. We are committed to minimizing impacts to the neighborhood, but will need community cooperation and understanding. Below are some images that convey information regarding parking, preferred truck routing and road closures.

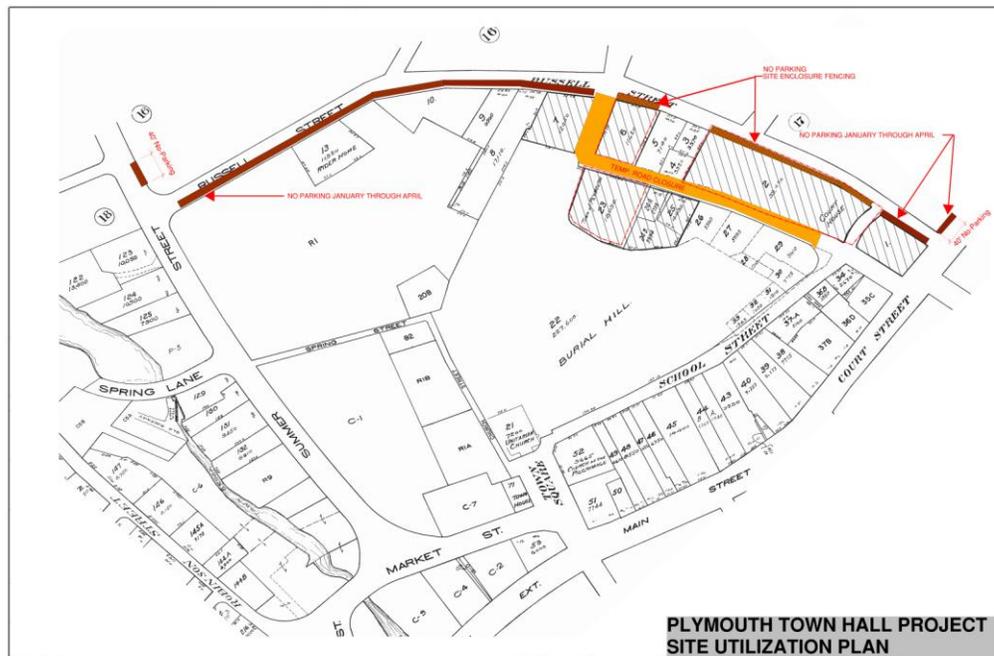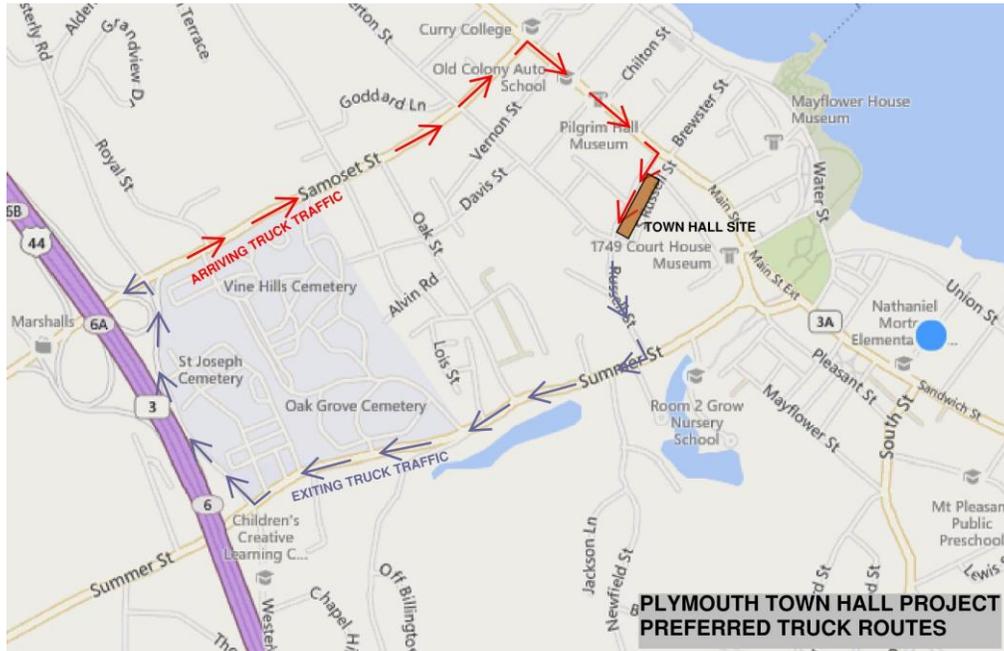

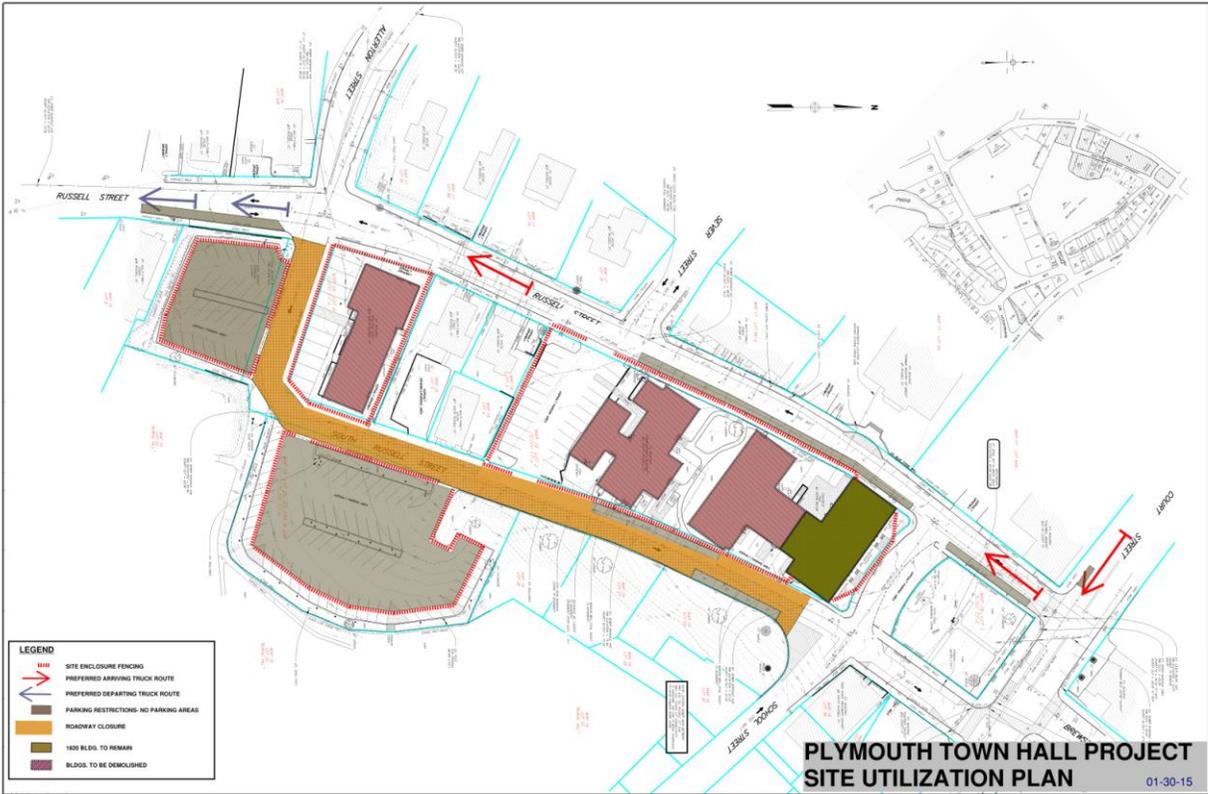


Demolition-Related Project Activities:

Week of January 19 th	Temporary Site Fencing Installation- Upper Site Area
Week of January 26 th	Mobilization @ DPW Sign Shop
Week of February 2 nd	Abatement Preparation, Containment and Abatement @ DPW Sign Shop
Week of February 16 th	Demolition of DPW Sign Shop (anticipated start)
Week of February 16 th	Site Remediation @ DPW and Upper Parking Area (anticipated start)
Week of February 16 th	Abatement Preparation, Containment and Abatement @ Commissioner's Building (anticipated start)
Week of February 23 rd	Demolition of Commissioner's Building (anticipated start)

Preliminary Project Images:

Schematic Site Plan

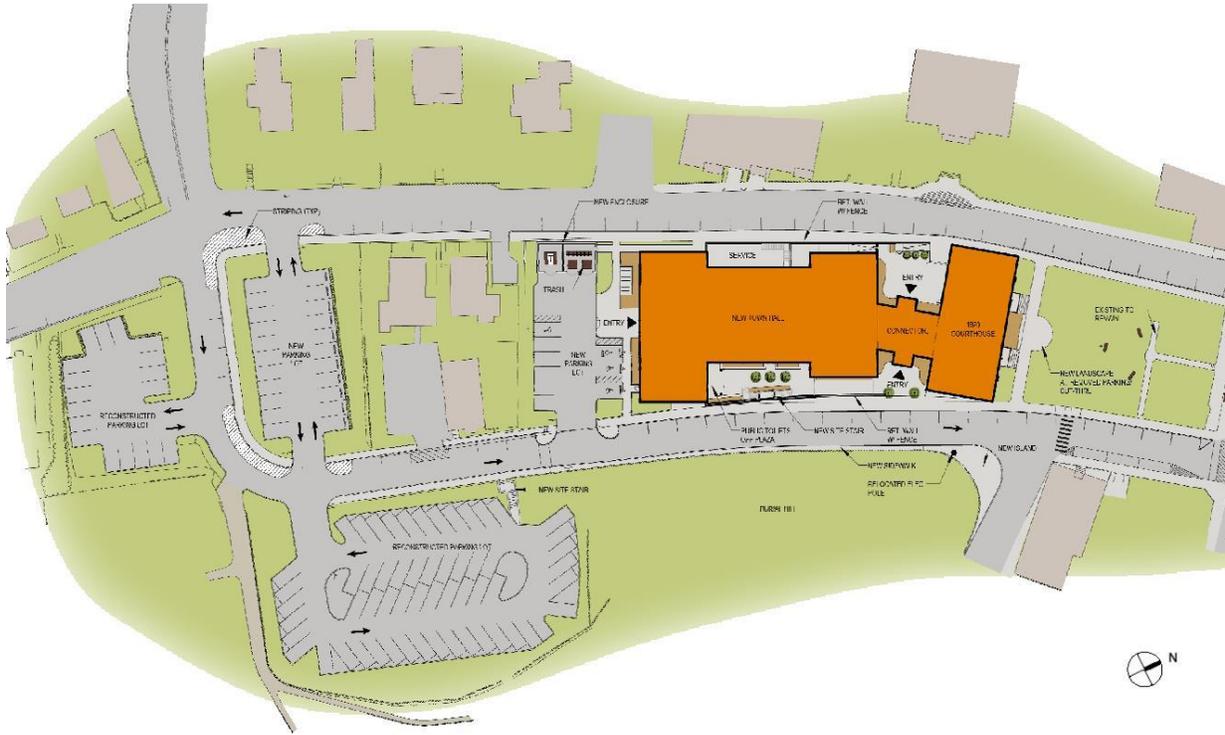

South Entrance



South Russell Street Entrance



Russel Street Entrance

Demolition Project Progress Photos-02-14-15-DPW Building:





Demolition Project Progress Photos-Week end 02-27-15:

DPW BUILDING/SITE



COMMISSIONER'S BUILDING/SITE





Demolition Project Progress Photos - 03-06-15 Commissioner's Building



Granite Salvage in Burial Hill



Three excavators Demoiing Commissioner's Building



Commissioner's Building Demo Complete



Saw Cut 1820 Courthouse

Demolition Project Progress Photos - March 13, 2015



Final Sawcut of 1884 Courthouse Addition - S Russell St.



Start of Demolition - 1962 Courthouse Addition



Start of Demolition - 1884 Courthouse Addition



Demolition Complete - Remainder to be Restored

Demo Project Progress Photos - Week End March 20, 2015



Courthouse Additions Demolished/Ready for Backfill



Commissioner's Bldg/Courthouse Backfilled and Compacted



DPW Site - Bulk Excavation Abatement Start



DPW Bulk Excavation - Wash Out Station Prior to Exiting Site

Demo Project Progress Photos - Week End March 27, 2015



Install of 1884 Addition Attic Weatherproof Sealant



Preparation of Additions Foundations for Removal



Backfill/Compaction of DPW Building Abatement Site



Rainwater Retention Basin at 1884 Additions Site

Demo Project Progress Photos - Week End April 3, 2015



Bulk Excavation Load Out at DPW Site



Backfill/Compaction at DPW Site



Public Works Subsurface Video Investigation Equipment



Public Works Employee Performing Subsurface Investigation to Locate Underground Pipe

Demo Project Progress Photos-Week End April 10, 2015



Final Grading at Cornish/DPW Lot



Bulk Load Out Into Long Distance Trailer Dumps - Burton School



Burton School Lot Nearing Completion of Bulk Load Out



**Wire Shields Being Removed and 8' Chain Link Fence Installed
South Russell Street (1820 Courthouse in Rear)**
