


Preliminary Schedule

Town of Plymouth

Emergency Wastewater Force Main Repairs

GC: Albanese D & S, Inc.

Engineer: Environmental Partners Group

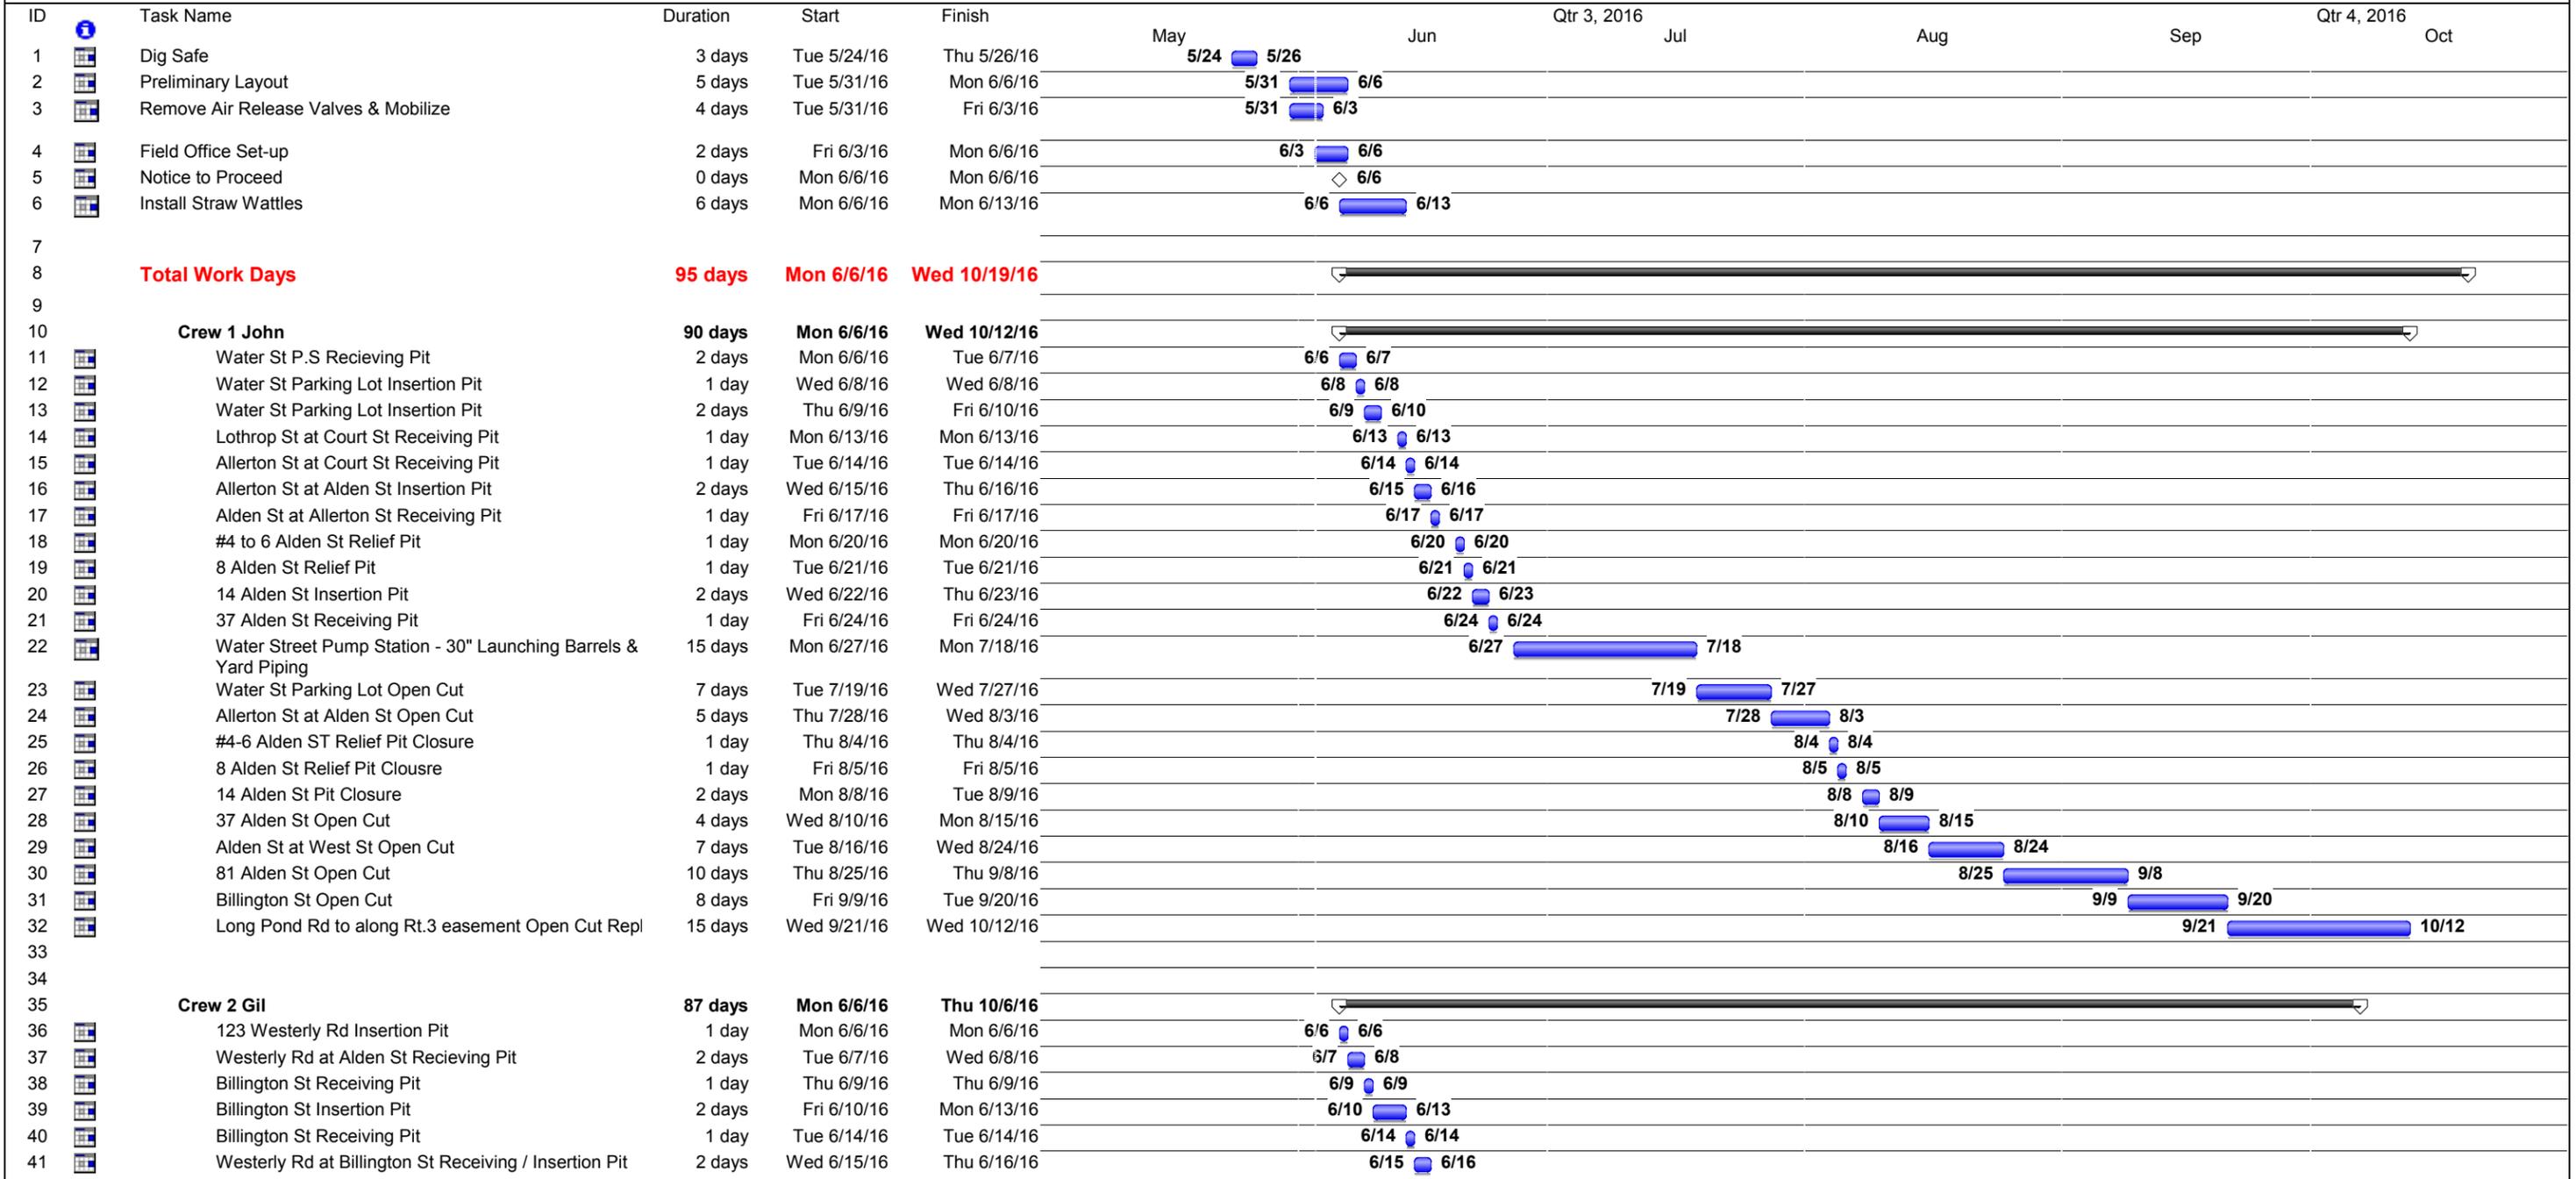

Project: Emergency Wastewater Force Main Date: Fri 6/3/16

Task [Blue Bar] Milestone [Diamond] Rolled Up Task [Blue Bar] Rolled Up Progress [Grey Bar] External Tasks [Grey Bar] Group By Summary [Dropdown]

Progress [Grey Bar] Summary [Dropdown] Rolled Up Milestone [Diamond] Split [Dotted Bar] Project Summary [Dropdown] Deadline [Green Arrow]

Schedule is based on availability of materials and is subject to change.
Paving, pressure testing and grouting will be on-going as soon as practical.

Preliminary Schedule

Town of Plymouth

Emergency Wastewater Force Main Repairs

GC: Albanese D & S, Inc.

Engineer: Environmental Partners Group



ID	Task Name	Duration	Start	Finish	May	Jun	Qtr 3, 2016	Jul	Aug	Sep	Qtr 4, 2016	Oct
42	81 Alden St Receiving Pit	1 day	Fri 6/17/16	Fri 6/17/16		6/17	6/17					
43	Alden St at West St Insertion Pit	2 days	Mon 6/20/16	Tue 6/21/16		6/20	6/21					
44	Alden St at West St Insertion Pit	2 days	Wed 6/22/16	Thu 6/23/16		6/22	6/23					
45	Court St from Lothrop St to Allerton St Open Cut	18 days	Fri 6/24/16	Wed 7/20/16		6/24	7/20					
46	123 Westerly Rd to Summer St Open Cut	55 days	Thu 7/21/16	Thu 10/6/16			7/21	10/6				
48	Crew 3 David	95 days	Mon 6/6/16	Wed 10/19/16								
49	Long Pond Rd to WWTP Open Cut Replacement including Flow Meter & Manhole	95 days	Mon 6/6/16	Wed 10/19/16		6/6	10/19					
51	Crew 4 ABI	85 days	Mon 6/20/16	Wed 10/19/16								
52	Westerly Rd at Billington St to Summer St Open Cut	25 days	Mon 6/20/16	Mon 7/25/16		6/20	7/25					
53	Billington St to along Rt. 3 easement Open Cut Replac	60 days	Tue 7/26/16	Wed 10/19/16			7/26	10/19				
55	Crew 5	25 days	Mon 6/13/16	Mon 7/18/16								
56	Fuse 24" HDPE Pipe	20 days	Mon 6/13/16	Mon 7/11/16		6/13	7/11					
57	Water St Parking Lot to Lothrop St at Court St Slipline	2 days	Mon 6/20/16	Tue 6/21/16		6/20	6/21					
58	Allerton St Slipline	2 days	Wed 6/22/16	Thu 6/23/16		6/22	6/23					
59	Billington St Slipline	2 days	Fri 6/24/16	Mon 6/27/16		6/24	6/27					
60	Westerly Rd to Billington St Slipline	2 days	Tue 6/28/16	Wed 6/29/16		6/28	6/29					
61	Water St Pump Station to Parking Lot Slipline	2 days	Thu 6/30/16	Fri 7/1/16		6/30	7/1					
62	Alden St Slipline	2 days	Tue 7/5/16	Wed 7/6/16		7/5	7/6					
63	Alden St Slipline	2 days	Thu 7/7/16	Fri 7/8/16		7/7	7/8					
64	Alden St Slipline	2 days	Mon 7/11/16	Tue 7/12/16		7/11	7/12					
65	Alden St Slipline	2 days	Wed 7/13/16	Thu 7/14/16		7/13	7/14					
66	Westerly Rd at Alden St to 123 Westerly Rd Slipline	2 days	Fri 7/15/16	Mon 7/18/16		7/15	7/18					

Project: Emergency Wastewater Force Main
Date: Fri 6/3/16

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary		Deadline	

Schedule is based on availability of materials and is subject to change.
Paving, pressure testing and grouting will be on-going as soon as practical.
